



**Kodiak
Asphalt Art
Initiative**



Implementation Plan

Table Of Contents

Project Schedule

03 Overall Schedule

Asphalt Art Site Plans

05 Pedestrian Plaza Plans **Day 1**

07 Pedestrian Plaza Plans **Day 2**

09 Curb Extension Plans **Day 3**

11 Curb Extension Plans **Day 4**


Transect Description &

Application Method

14 Transect Description

15 Application Diagram

Project Schedule (Overall)

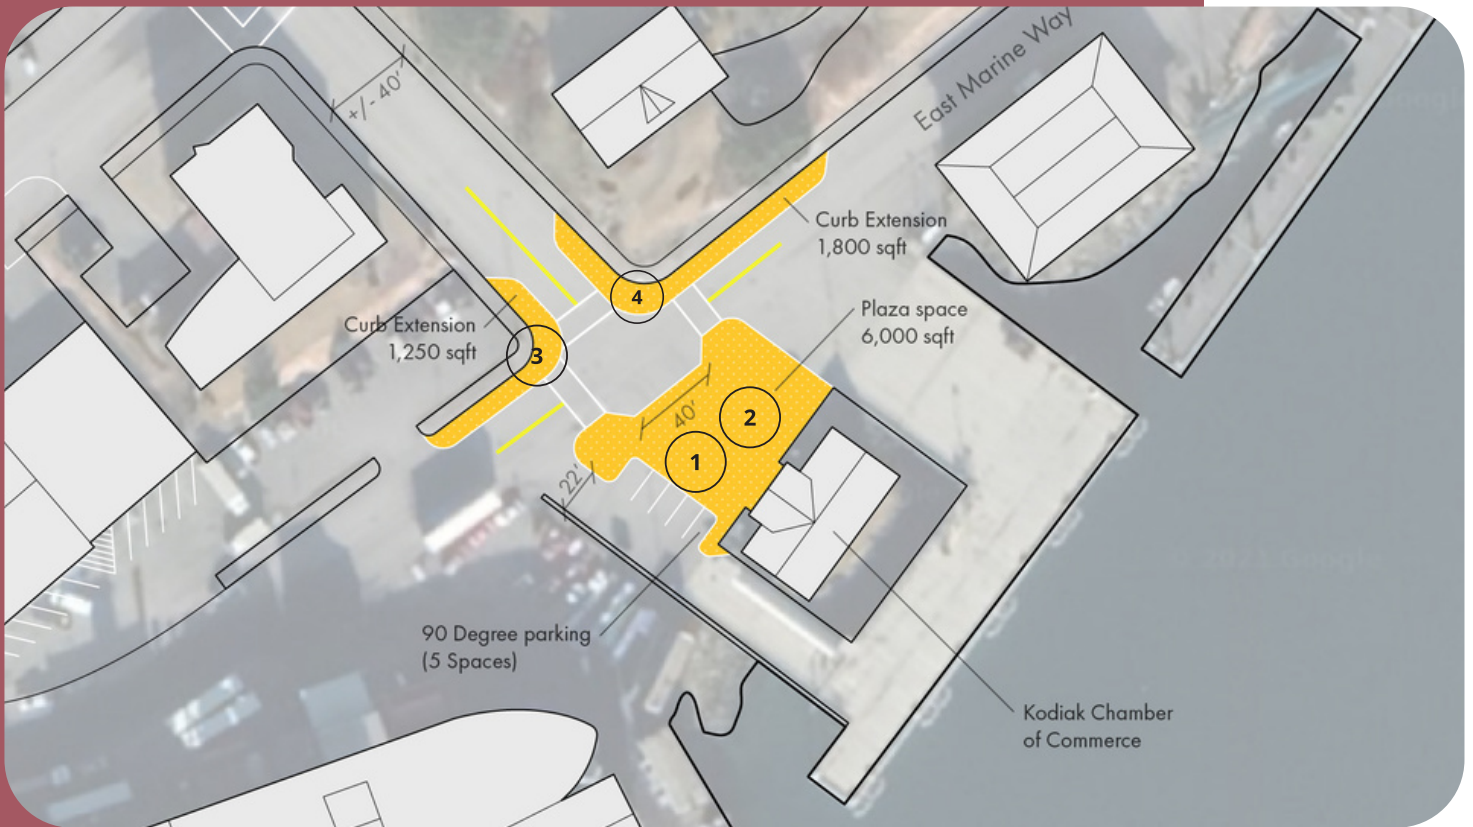

1

Day 1 - Monday 8 Aug

Pedestrian Plaza
Kodiak Visitor's Center/Chamber of
Commerce/Ferry Terminal

2

Day 2 - Tuesday 9 Aug

Pedestrian Plaza
Kodiak Visitor's Center/Chamber of
Commerce/Ferry Terminal

3


Day 3 - Wednesday 10 Aug

Curb Extension
KNWR Side

4

Day 4 - Thursday 11 Aug

Curb Extension
KHM Side



Asphalt Art Site Plans

Day 1 Pedestrian Plaza



Sun Team

Bonnie Dillard
3 Volunteers



Bear Team

Lynn Walker
4 Volunteers



Salmon Team

Marina Thomas &
Bonnie Dillard
3 Volunteers

Start

7:00AM Storage Pickup
7:30AM Set-Up & Training
8:00AM Stencil Placement & Outlining
(Teams 1 & 2)
9:00AM Paint (Teams 1 & 2)
10:30AM Outline & Paint Details
(Teams 1 & 2)
Noon Lunch
1:00PM Stencil Placement & Outlining
(Team 3)
2:00PM Paint (Team 3)
3:30PM Outline & Paint Details (Team 3)
5:00PM Breakdown
5:30PM Storage Drop-Off
End

Day 2 Pedestrian Plaza

1

Cloud Team

Bonnie Dillard
4 Volunteers

2

Raindrop & Puddle Team

Marina Thomas
4 Volunteers

3

Accent Team

Lynn Walker
3 Volunteers

Start

7:00AM Storage Pickup

7:30AM Set-Up & Training

8:00AM Stencil Placement & Outlining
(Teams 1 & 2)

9:00AM Paint (All Teams)

10:30AM Outline & Paint Details
(All Teams)

Noon Lunch

1:00PM Paint Details & Final Touches

3:00PM Sealant Coat

4:00PM Breakdown

4:30PM Storage Drop-Off

End

Day 3 Curb Extension (KNWR)



Border Team

Lynn Walker
4 Volunteers



Salmon Team

Marina Thomas
4 Volunteers



Bear & Raven Team

Bonnie Dillard
3 Volunteers

Start

- 7:00AM Storage Pickup
 - 7:30AM Set-Up & Training
 - 8:00AM Stencil Placement & Outlining (Team 1)
 - 9:00AM Paint (Team 1)
 - 10:30AM Stencil Placement & Outlining (Teams 2 & 3)
 - Noon Lunch
 - 1:00PM Outline & Paint (Teams 2 & 3)
 - 2:30PM Outline & Paint Details (Teams 2 & 3)
 - 4:00PM Sealant Coat
 - 4:30PM Breakdown
 - 5:00PM Storage Drop-Off
- End

Day 4 Curb Extension (KHM)



Border Team

Lynn Walker
4 Volunteers



Salmon Team

Marina Thomas
4 Volunteers



Bear & Raven Team

Bonnie Dillard
3 Volunteers

Start
7:00AM Storage Pickup
7:30AM Set-Up & Training
8:00AM Stencil Placement & Outlining
(Team 1)
9:00AM Paint (Team 1)
10:30AM Stencil Placement & Outlining
(Teams 2 & 3)
Noon Lunch
1:00PM Outline & Paint (Teams 2 & 3)
2:30PM Outline & Paint Details
(Teams 2 & 3)
4:00PM Sealant Coat
4:30PM Breakdown
5:00PM Storage Drop-Off
End



Transect Descriptions & Stencil Application

Transect Descriptions



Pedestrian Plaza

Brown Bears
Salmon
Ravens
Clouds
Sun

Curb Extension (KNWR)

Brown Bear
Salmon



Curb Extension (KHM)

Ravens
Salmon



Stencil Application Flow Chart

Step 1

Position stencil.

Step 2

Paint stencil and let dry.

Step 3

For bears and salmon: arrange details using chalk.

Step 4

For bears and salmon: paint details and let dry.

Step 5

Apply sealant layer.

Materials:

- Paint: yellow, black, white, red
- Rollers, brushes, paint trays, liners (paint pail and tray)
- Chalk
- Stencils
